MR BCT Meeting July 19, 2006 at 1:30 p.m.

Item	Action	Comment
Fieldwork Update	Update	
Site Security Program	Update	
MRS-16	Update	
Report Status	Update	
Property Transfer	Update	
Tracks 0/1	Status Update	
Track 2	Status Update	
Track 3	Update	
Report status / 90-day upcoming reports	Status Update	
FFA Schedule	Update	
Action Items	Update	

SUBJECT: MK BCT Meeting July 19, 2006 1:30 p.m. BRAC Conference Room

Check	Name	Organization	Phone	E-mail address
Glej	Gail Youngblood	Fort Ord BRAC	831-242-7918	Gail.youngblood@monterey.army.mil
RB	Roman Racca	DTSC	916-255-6407	Rracca@dtsc.ca.gov
	Stewart Black	DTSC	916-255-3665	sblack@dtsc.ca.gov
	John Chesnutt	U.S. EPA	415-972-3005	Chesnutt.john@epa.gov
Q	Claire Trombadore	U.S. EPA	415-972-3518	Trombadore.Claire@epa.gov
y phone	Christopher Cora	U.S. EPA	415-972-3518	Cora.Christopher@epamail.epa.gov
7	David Eisen	COE	831-393-9692	David.Eisen@usace.army.mil
here	Bruce Wilcer	Harding ESE	415-884-3168	blwilcer@mactec.com
CA	Chieko Nguyen	Fort Ord BRAC	831-899-7372	Chieko.nguyen@monterey.army.mil
W	Lyle Shurtleff Fort Ord BRAC		831-242-7919	Lyle.Shurtleff@monterey.army.mil
	Derek Lieberman	Fort Ord BRAC	831-242-4873	Derek.Lieberman@monterey.army.mil
	Jennifer Payne	COE		Jennifer.J.Payne@usace.army.mil

SUBJECT: MK BCT Meeting July 19, 2006 1:30 p.m. BRAC Conference Room

Check	Name	Organization	Phone	E-mail address
AR P	Christopher Prescott	COE	916-557-7227	Christopher.E.Prescott@usace.army.mil
	George Siller	COE	916/557-7418	George.L.Siller@usace.army.mil
	Kris Escarda	DTSC	916-255-3651	kescarda@dtsc.ca.gov
M	Peter Kelsall	Shaw E&I	831-883-5810	Peter.Kelsall@shawgrp.com
KS5	Kevin Siemann	Shaw E&I	831-883-0103	Kevin.Siemann@shawgrp.com
033	Cynthia Burris	USACE	916-557-6745	Cynthia.S.Burris@usace.army.mil
	Chris Duymic	h POMED	242-7701	Chris. duymich@monterer
				7

Military Munitions Response Fieldwork Program Fort Ord Update

MMRP Fieldwork Update MRS-16

The 79 acre area of MRS-16 have been prepared and surveyed for vegetation removal (prescribed burn) in preparation for a removal to depth munitions response. USF&W has concurred with the a plan described in the project preparation description for establishment of a primary prescribed burn containment line involving 22.5 acres of CMC with a one-time vegetation cut and subsequent blacklining. Habitat management transects have been installed to support monitoring of vegetation recovery from the planned preparatory, prescribed burn, and munitions response actions. Voluntary temporary relocation will be offered for this prescribed burn (1). Fuel moisture monitoring is in progress (2). Weather monitoring is in progress (3). Vegetation cutting and other preparatory work is complete. Air monitoring is planned for this prescribed burn. The draft work plan is out for comment. The notification list for this prescribed burn is complete.

PHASES:

Start Date Da

Date Complete

Preparatory Actions

6-19-06

7-12-06

Prescribed burn

Surface safety sweep

Vegetation removal (remainder)

Digital survey

Subsurface removal

Digital survey/QC/QA

ISSUES AND CONCERNS:

- (1) Voluntary temporary relocation signup period is complete.
- (2) Average fuel moisture is 104% as of 7-17-06. Maximum prescribed average fuel moisture is 100%.
- (3) Weather prediction is unfavorable for burn prescription through 7-20-06.

7/19/2006

MMRP Fieldwork Update

PROJECT: Range 36A

The munitions response for Range 36A is in progress. The vegetation on the 1.8-acre area of Range 36A was removed (cut) in preparation for the munitions response action. A digital (EM-61) survey of the area has identified significant subsurface anomalies. One range-related debris item has been treated (wholly inert 250-pound General Purpose practice bomb). Excavation of peak subsurface anomalies is complete. Request for extension of closure period and proposal to amend Closure Plan (Munitions Response Work Plan) has been submitted. Further work is pending DTSC letter to grant extension for closure and comment to Army's proposed action plan.

Start date: 5-2-06

Estimated date complete: TBD

PHASES:

Surface safety sweep	Complete
Vegetation removal	Complete
Digital survey	Complete
Subsurface sampling (peak anomalies)	Complete
Closure Plan Amendment	In progress

ISSUES AND CONCERNS:

1) High density of subsurface anomalies.

MMRP Fieldwork continued

PROJECT: Annual Impact Area Fuel Break Maintenance

Start Date: 7/06

Estimated date complete: 9/06

PHASES: Vegetation cut on existing fuel breaks adjacent to and within the impact area (MRS-BLM) (approx. 245 acres).

Issues and Concerns:

(1) Funding and contractor

7/19/2006

MMRP Fieldwork Update Unexploded Ordnance (UXO)/Munitions Debris (MD)/ Range Related Debris (RRD) Summary

Description	UXO/DMM/TBD	<u>MD</u>	RRD
	(Items)	<u>(lbs.)</u>	(lbs.)
MRS-16	0/0/6	10	2,010
Range 36A	0/0/0	0	250
SBR	0/0/0	()	10

MMRP Site Security Program


Trespass and MEC Incidents


- Trespass Incidents: None
- MEC Incidents (Reports):
 - None

Community Education: None


Other: 2005 MRS Security Annual Report is pending publication.

7/19/2006

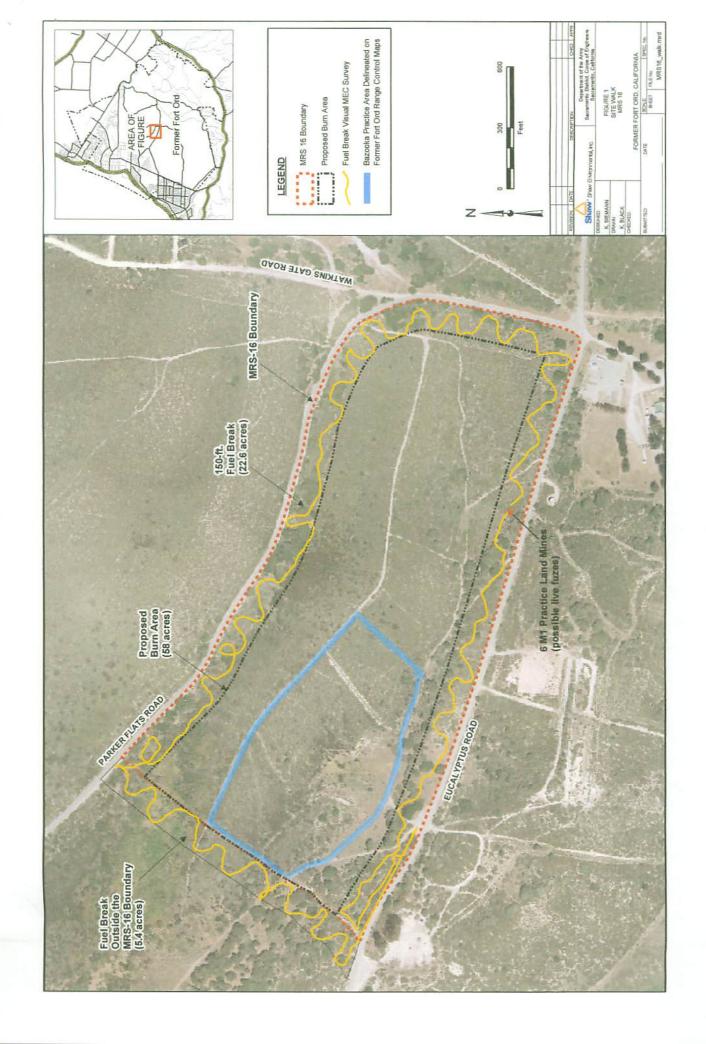

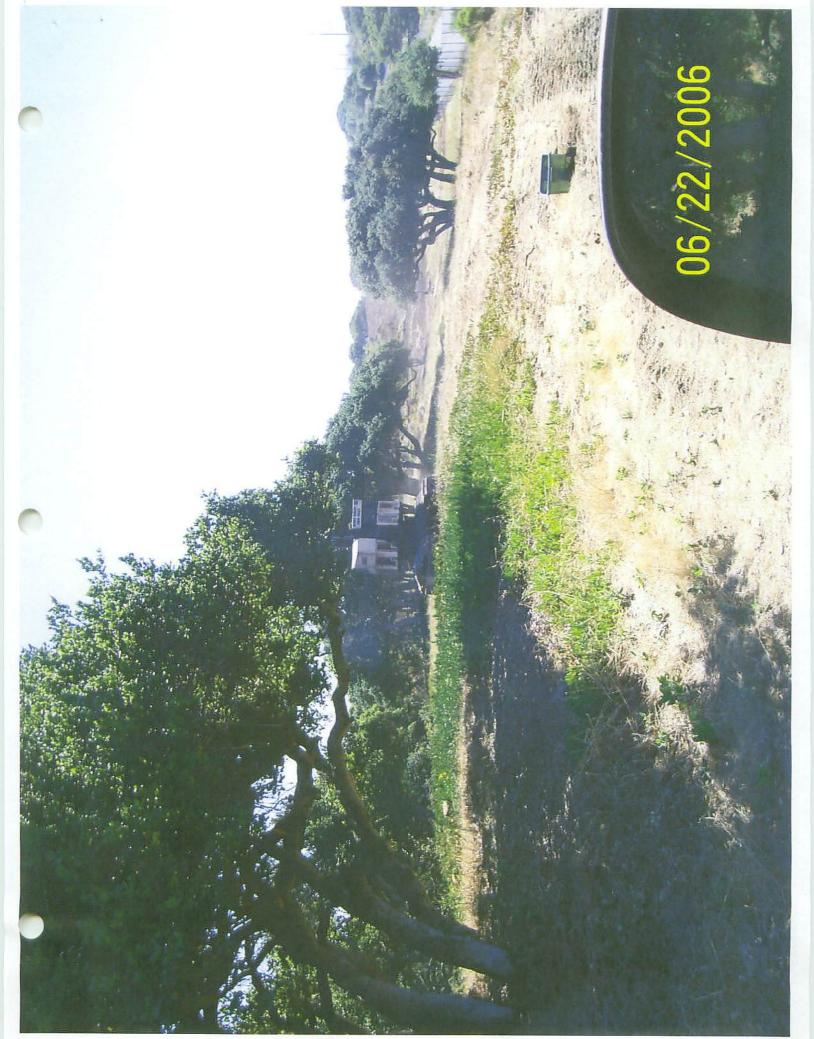



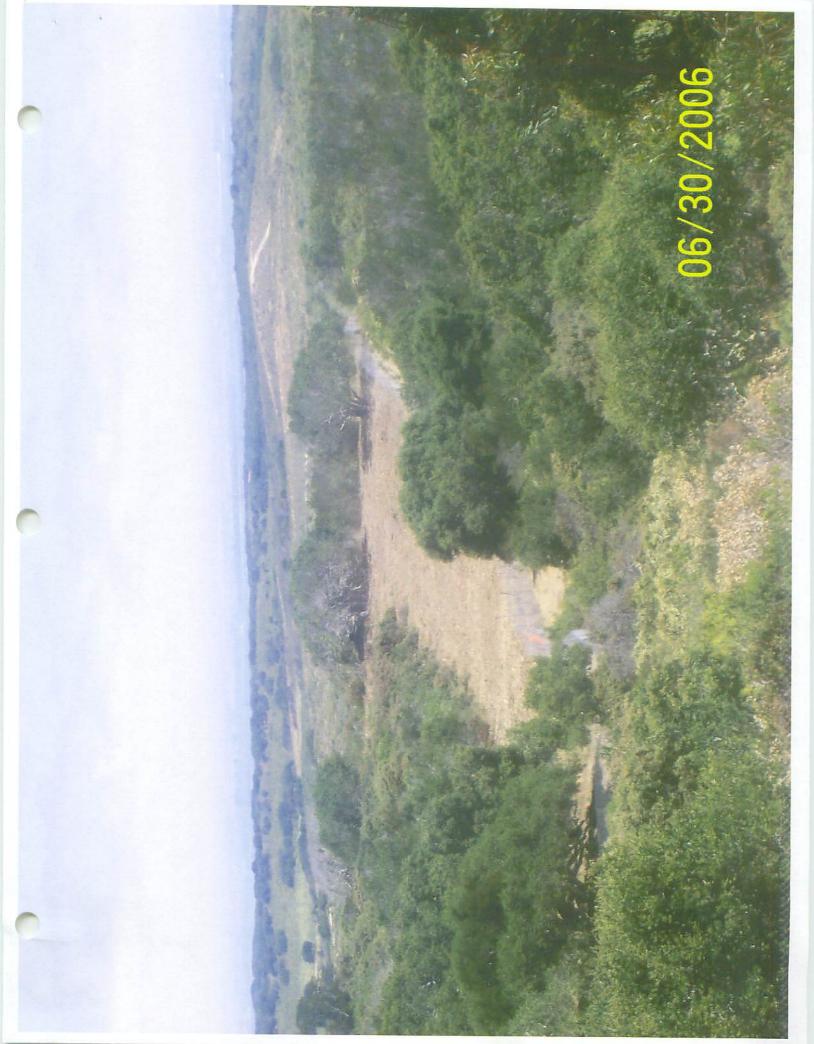

Grouping	<u>Site</u>	Activity	<u>Deliverable</u>	Proposed Issue Date	Issue Date Status	Agency Comments Due	Company	Author	Status
Primary FFA Documents	Basewide	Miscellaneous	Final Community Relations Plan, Update Number 3	Jun-23-06	issued		Dept of Army		
Other Documents (Non-CERCLA)	EBS/FOST	FOSET	Draft FOSET 5 (agency review only)	Jan-17-06	issued	Feb-24-06	MACTEC E&C	J, Fenion	EPA comments rec'd 2/23.
Other Documents (Non-CERCLA)	EBS/FOST	FOSL	Final MPC MOUT Site FOSL, Version 2 (signature process)	May-16-06	issued		MACTEC E&C	J, Fenton	
Other Documents (Non-CERCLA)	EBS/FOST	FOST	Draft FOST 10 (agency review only)	May-26-06	issued	Jun-27-06	MACTEC E&C	J, Fenton	EPA and DTSC comments rec'd 6/27,
Other Documents (Non-CERCLA)	EBS/FOST	FOST	Draft Final FOST 10 (public review period)	Jul-28-06		Aug-28-06	MACTEC E&C	J. Fenton	
Other Documents (Non-CERCLA)	EBS/FOST	FOST	Final FOST 10 (agency concurrence)	Sep-04-06		Sep-18-06	MACTEC E&C	J, Fenton	
Other Documents (Non-CERCLA)	EBS/FOST	FOST	Final FOST 10 (signature process)	Sep-19-06			MACTEC E&C	J. Fenton	
Secondary Documents	OE	Supporting Reports	Draft Final Prescribed Burn Supplemental Report Ranges 43-48	Jan-27-06	issued	Mar-02-06	MACTEC E&C	D, Leibensberger/B. Wilcer	Comment rec'd from MBUAPCD 3/2/06, FOEJN 3/3/06.
Primary FFA Documents	OE	Record of Decision	n Final Track 1 Plug-in Approval Memo, East Garrison Areas 2 and 4 NE (agency concur)	May-22-06	issued		Parsons/Dept of Army	Not Indicated	Army Itr 5/22 requested agency condurrence by 6/5, EPA concurrence Itr 6/1, DTSC concurrence Itr dated 5/30 rec'd 6/8/06.
latinggyasis. Million is	(a) ÷	SESSION DE		(10%5C)	Win in	UniXXII	11 E 20	nđờ - z	129, Angewordt gelekting fallegen (de 1975) Berlied er hat 187, Angewordte (d. 1972) Geografia (d. 1972)
Primary FFA Documents	OE	Supporting Reports	Draft Interim Action MR Technical Information Paper, R43-48.	May-30-06	issued	Jul-20-06	Parsons, Inc.	Not Indicated	EPA and DTSC requested extension till 7/20/06,
चित्रमें अस्ति व १९५५ व्याप	0).	TROPESTON Investigation	og og en er statistisk for den Eller († 15. Eksterner († 15. juni 16. juni Eksterner († 16. juni	gaga anga			Weise 10		PSEAN SEAN SEARCH CHARLES PROGRAMMENTO SEAN THE PROGRAMMENT SEASON SEASO
Primary FFA Documents	OE	Work Plan	Draft Final Work Plan MRS-16 MEC Removal, Rev 0	Jun-02-06	issued	Jul-05-06	Shaw E&I	Not Indicated	EPA comments rec'd 7/5, FOEJN comments rec'd 7/10, DTSC comments rec'd 7/13,
Secondary Documents	OE	After Action Reports	Drail Final Non-TCRA MRS-MOCO,2 After Action Report	Jun-06-06	issued	Jul-11-06	Parsons	Not Indicated	
Primary FFA Documents	OE	Record of Decision	Final Track 0 Plug-in Approval Memorandum, Group D (for agency concurrence)	Jun-15-06	no revision required		FI Ord BRAC/MACTEC	Not Indicated	No comments rec'd; Army requested agency concurrence 6/15/06, EPA concurred 6/27, DTSC concurred on 7/13/06,
Primary FFA Documents	OU 2	Landfill Activities	Final OU2 ESD MEC Issues, LFG, Reuse of Treated Groundwater (Army staffing process)	Jun-20-06	issued	Jul-07- 0 6	Dept, of Army	D, Lieberman	ESD was updated based on agency comments on 5/10 backcheck version.
Primary FFA Documents	OE	Work Plan	Draft Final Work Plan MRS-16 MEC Removal, Rev 0 - ADDENDUM (Appendix M Relocation/Notification Plan)	Jun-27-08	issued	Jul-10-06	Shaw E&I	Not Indicated	FOEJN comments rec'd 7/10/06,
ele geere Mysterer		V.P.S.E.THEFT		0,472,53		્રા કર્જાસ્ટ્ર <u>ું</u>	FEIR	[:\s]	્રાંતાના પુરુષાના પંચાયતઘર પ્રાપ્ય વધા છે. પ્રાપ્ય પ્રાપ્ય

90-day Upcoming Document List MMRP Created from Decument Deliverables Schedule of 777/06

Grouping	Site	Activity	Deliverable	Proposed Issue Date	Issue Date Status	Agency Comments	Company	Author	Status
Primary FFA Documents	a a	Record of Decision	Record of Decision Final Track 1 Plug-in Approval Memo Multiple Sites, Groups 1-5 (agency concurrence)	Jul-18-08			MACTEC E&C	J. Fenton	EPA comments on public review version recid 6/27, FOEJN comments recid 7/8/06,
Primary FFA Documents	꽁	Remedial Investigation	Draft Track 3 Impact Area MR RVFS Report	Jul-31-06		Sep-29-06	MACTEC E&C	Not Indicated	
Primary FFA Documents	Ä	Supporting Reports	Draft Final Interim Action MR Technical Information Paper, R43-48	Aug-03-06		Sep-02-06	Parsons, Inc.	Not Indicated	
Primary FFA Documents	96 6	Record of Decision	Record of Decision Draft Track 2 Record of Decision (Parker Flats)	Aug-11-08		Sep-10-06	MACTEC E&C	Not Indicated	
Primary FFA Documents	9	Record of Decision	Record of Decision Draft Final Track 2 Record of Decision (Parker Flats)	Sep-25-06		0ct-10-06	MACTEC E&C	Not indicated	
Secondary Documents	.	Reports	Draff Ordnance Detonation Air Modeling Report		TBD		TBD	TB O	
Secondary Documents	9	Reports	Draft Ordnance Detonation Sampling Report		OET		180	180	
Secondary Documents	OE.	Reports	Draft Final Ordnance Detonation Sampling Report	ı	T B0		ТВО	Œ	

Late reports
Blue text Updated dates

Interim Action Remedial Design/Remedial Action Former Fort Ord DRAFT

Draft After Action Burn Report Ranges 43-48 4/04	Deliverable/Event	Current Deadlines	Deadline Revision Rationale
Comments Due 5004	Draft After Action Burn Report Ranges 43-48	4/04	<u> </u>
Comments Due		5/04	
Comments Due	Draft Final After Action Burn Report Ranges 43-48	6/04	
Ranges 43-48 Comments Due Taft Final Interim Action MR After Action Report MRS-16 Comments Due Taft Final Interim Action MR After Action Report MRS-16 Comments Due Tab Tab Comments Due Tab Comments Due Tab Tab Comments Due Tab Tab Tab Comments Due Tab Tab Tab Tab Tab Tab Tab Ta		7/04	
Extended based on agency request. Draft Final Interim Action MR Technical Information Paper Ranges 43-48 Comments Due Profit Site Specific Plans for MRS-16 Comments Due Profit Site Specific Plans for MRS-16 Comments Due Profit Site Specific Plans for MRS-16 Comments Due Profit Final Site Specific Plans for MRS-16 Comments Due Profit Final Site Specific Plans for MRS-16 Comments Due Profit Final After Action Burn Report MRS-16 Comments Due Profit Final After Action Burn Report MRS-16 Comments Due Profit Final After Action Report MRS-16 Comments Due Profit Final Interim Action MR After Action Report MRS-16 Comments Due Profit Final Interim Action MR After Action Report MRS-16 Comments Due Profit Final Site Specific Plans for Range 30A TBD Traft Final Site Specific Plans for Range 30A TBD Profit Final Site Specific Plans for Range 30A TBD Profit Final After Action Burn Report Range 30A TBD Comments Due TBD Profit Final After Action Burn Report Range 30A TBD Comments Due TBD Profit Final After Action Burn Report Range 30A TBD Comments Due TBD Profit Final After Action MR After Action Report Range 30A TBD Comments Due TBD Profit Final After Action MR After Action Report Range 30A TBD Comments Due TBD Profit Final Interim Action MR After Action Report Range 30A TBD Comments Due TBD Profit Final Interim Action MR After Action Report Range 30A TBD Comments Due TBD Profit Final Interim Action MR After Action Report Range 30A TBD Comments Due TBD TBD TBD TBD TBD TBD TBD TBD		5/06	
Paper Ranges 43-48	Comments Due	7/06 (6/06)	extended based on
Draft Site Specific Plans for MRS-16		8/06 (7/06)	Reflects change above.
Comments Due	Comments Due	9/06 (8/06)	i.
Comments Due	Draft Site Specific Plans for MRS-16	3/06	
Draft Final Site Specific Plans for MRS-16 Comments Due Traft After Action Burn Report MRS-16 Comments Due Traft Final After Action Burn Report MRS-16 Comments Due Traft Interim Action MR After Action Report MRS-16 Comments Due Traft Final Interim Action MR After Action Report MRS-16 Comments Due Traft Final Interim Action MR After Action Report MRS-16 Comments Due Traft Final Interim Action MR After Action Report MRS-16 Comments Due Traft Site Specific Plans for Range 30A TBD Comments Due TBD Draft Final Site Specific Plans for Range 30A TBD Comments Due TBD Draft After Action Burn Report Range 30A TBD Comments Due TBD Draft After Action Burn Report Range 30A TBD Traft Final After Action Burn Report Range 30A TBD Traft Final After Action Burn Report Range 30A TBD Traft Final After Action Burn Report Range 30A TBD Traft Final After Action Burn Report Range 30A TBD Traft Final After Action Burn Report Range 30A TBD Traft Final After Action Report Range 30A TBD Traft Interim Action MR After Action Report Range 30A TBD Traft Final Interim Action MR After Action Report TBD Traft Final Interim Action MR After Action Report TBD Traft Final Interim Action MR After Action Report TBD Traft Final Interim Action MR After Action Report TBD Traft Final Interim Action MR After Action Report TBD Traft Final Interim Action MR After Action Report TBD			
Draft After Action Burn Report MRS-16			
Draft After Action Burn Report MRS-16 Comments Due 3/07 Draft Final After Action Burn Report MRS-16 Comments Due 5/07 Draft Interim Action MR After Action Report MRS-16 Comments Due 5/07 Draft Final Interim Action MR After Action Report MRS-16 Comments Due 5/07 Draft Final Interim Action MR After Action Report MRS-16 Comments Due 7/07 Draft Site Specific Plans for Range 30A TBD Comments Due TBD Draft Final Site Specific Plans for Range 30A TBD Draft After Action Burn Report Range 30A TBD Comments Due TBD Draft After Action Burn Report Range 30A TBD Comments Due TBD Draft Final After Action Burn Report Range 30A TBD Comments Due TBD Draft Interim Action MR After Action Report Range 30A Comments Due TBD Draft Interim Action MR After Action Report Range 30A TBD			
Comments Due 3/07 Draft Final After Action Burn Report MRS-16 4/07 Comments Due 5/07 Draft Interim Action MR After Action Report MRS-16 Comments Due 5/07 Draft Final Interim Action MR After Action Report MRS-16 Comments Due 7/07 MRS-16 Comments Due 7/07 Draft Site Specific Plans for Range 30A TBD Comments Due TBD Draft Final Site Specific Plans for Range 30A TBD Comments Due TBD Draft After Action Burn Report Range 30A TBD Comments Due TBD Draft Final After Action Burn Report Range 30A TBD Comments Due TBD Draft Final After Action Burn Report Range 30A TBD Comments Due TBD Draft Interim Action MR After Action Report Range 30A TBD Comments Due TBD Draft Interim Action MR After Action Report Range TBD Draft Interim Action MR After Action Report Range TBD Draft Final Interim Action MR After Action Report TBD Draft Final Interim Action MR After Action Report TBD Draft Final Interim Action MR After Action Report TBD Draft Final Interim Action MR After Action Report TBD Draft Final Interim Action MR After Action Report TBD Draft Final Interim Action MR After Action Report TBD	Comments Duc	7700	
Comments Due 3/07	Draft After Action Burn Report MRS-16	2/07	
Draft Final After Action Burn Report MRS-16 Comments Due 5/07 Draft Interim Action MR After Action Report MRS-16 Comments Due 5/07 Draft Final Interim Action MR After Action Report MRS-16 Comments Due 7/07 Draft Site Specific Plans for Range 30A Comments Due TBD Draft Final Site Specific Plans for Range 30A TBD Comments Due TBD Draft Final Site Specific Plans for Range 30A TBD Comments Due TBD Draft After Action Burn Report Range 30A TBD Comments Due TBD Draft Final After Action Burn Report Range 30A TBD Comments Due TBD Draft Interim Action MR After Action Report Range 30A TBD Comments Due TBD Draft Interim Action MR After Action Report Range 30A TBD TBD Draft Interim Action MR After Action Report Range 30A TBD TBD Draft Final Interim Action MR After Action Report Range 30A TBD TBD Draft Final Interim Action MR After Action Report TBD Draft Final Interim Action MR After Action Report TBD Draft Final Interim Action MR After Action Report TBD Draft Final Interim Action MR After Action Report TBD		3/07	
Comments Due 5/07 Draft Interim Action MR After Action Report MRS- 16 Comments Due 5/07 Draft Final Interim Action MR After Action Report 6/07 MRS-16 Comments Due 7/07 Draft Site Specific Plans for Range 30A TBD Comments Due TBD Draft Final Site Specific Plans for Range 30A TBD Comments Due TBD Draft After Action Burn Report Range 30A TBD Comments Due TBD Draft Final After Action Burn Report Range 30A TBD Comments Due TBD Draft Final After Action Burn Report Range 30A TBD Comments Due TBD Draft Interim Action MR After Action Report Range 30A TBD Comments Due TBD Draft Interim Action MR After Action Report Range 30A TBD Draft Interim Action MR After Action Report Range 30A TBD TBD Draft Final Interim Action MR After Action Report Range 30A TBD Draft Final Interim Action MR After Action Report Range 30A TBD Draft Final Interim Action MR After Action Report TBD		4/07	
Draft Interim Action MR After Action Report MRS- 16 Comments Due 5/07 Draft Final Interim Action MR After Action Report MRS-16 Comments Due 7/07 Draft Site Specific Plans for Range 30A Comments Due TBD Draft Final Site Specific Plans for Range 30A TBD Comments Due TBD Draft After Action Burn Report Range 30A TBD Comments Due TBD Draft Final After Action Burn Report Range 30A TBD Comments Due TBD Draft Final After Action Burn Report Range 30A TBD Comments Due TBD Draft Interim Action MR After Action Report Range 30A TBD TBD Draft Interim Action MR After Action Report Range 30A TBD TBD TBD TBD TBD TBD TBD TBD			
Draft Final Interim Action MR After Action Report MRS-16 Comments Due 7/07 Draft Site Specific Plans for Range 30A Comments Due TBD TBD TBD TBD TBD TBD TBD TB	Draft Interim Action MR After Action Report MRS-		
Draft Final Interim Action MR After Action Report MRS-16 Comments Due 7/07 Draft Site Specific Plans for Range 30A Comments Due TBD TBD TBD TBD TBD TBD TBD TB	Comments Due	5/07	
Draft Site Specific Plans for Range 30A Comments Due TBD TBD Draft Final Site Specific Plans for Range 30A Comments Due TBD Draft After Action Burn Report Range 30A TBD Comments Due TBD Draft Final After Action Burn Report Range 30A TBD TBD Draft Final After Action Burn Report Range 30A TBD TBD TBD Draft Interim Action MR After Action Report Range 30A TBD TBD TBD TBD TBD TBD TBD TB		6/07	
Comments Due Draft Final Site Specific Plans for Range 30A Comments Due TBD Draft After Action Burn Report Range 30A Comments Due TBD Draft Final After Action Burn Report Range 30A TBD Comments Due TBD Draft Interim Action MR After Action Report Range 30A TBD TBD TBD TBD TBD TBD TBD TB	Comments Due	7/07	
Comments Due Draft Final Site Specific Plans for Range 30A Comments Due TBD Draft After Action Burn Report Range 30A Comments Due TBD Draft Final After Action Burn Report Range 30A TBD Comments Due TBD Draft Interim Action MR After Action Report Range 30A TBD TBD TBD TBD TBD TBD TBD TB			
Draft Final Site Specific Plans for Range 30A Comments Due TBD TBD TBD Draft After Action Burn Report Range 30A Comments Due TBD Draft Final After Action Burn Report Range 30A TBD Comments Due TBD Draft Interim Action MR After Action Report Range 30A TBD TBD TBD TBD TBD TBD TBD TB			
Comments Due Draft After Action Burn Report Range 30A Comments Due TBD TBD TBD TBD TBD TBD Comments Due TBD Comments Due TBD TBD TBD TBD TBD TBD TBD TB			
Draft After Action Burn Report Range 30A Comments Due TBD Draft Final After Action Burn Report Range 30A Comments Due TBD Draft Interim Action MR After Action Report Range 30A Comments Due TBD TBD TBD TBD TBD TBD TBD TB			
Comments Due Draft Final After Action Burn Report Range 30A Comments Due TBD Draft Interim Action MR After Action Report Range 30A Comments Due TBD TBD TBD TBD TBD TBD TBD TB	Comments Due	TBD	
Comments Due Draft Final After Action Burn Report Range 30A Comments Due TBD Draft Interim Action MR After Action Report Range 30A Comments Due TBD TBD TBD TBD TBD TBD TBD TB	Draft After Action Burn Report Range 30A	TBD	
Draft Final After Action Burn Report Range 30A Comments Due Draft Interim Action MR After Action Report Range 30A Comments Due TBD TBD TBD TBD TBD TBD TBD TB			
Comments Due Draft Interim Action MR After Action Report Range 30A Comments Due TBD TBD TBD Draft Final Interim Action MR After Action Report Range 30A			
Draft Interim Action MR After Action Report Range 30A Comments Due TBD Draft Final Interim Action MR After Action Report Range 30A TBD			
Comments Due TBD Draft Final Interim Action MR After Action Report Range 30A TBD	Draft Interim Action MR After Action Report Range		
Draft Final Interim Action MR After Action Report Range 30A TBD		TBD	
	Draft Final Interim Action MR After Action Report		
		TBD	

Draft Track 2, Former Fort Ord

Deliverable/Event	Current Deadlines	Deadline Revision Rationale
Track 2		
Draft Final OE Remedial Investigation/Feasibility Study Workplan	5/00	
Comments Due	6/00	
Draft OE Sampling and Analysis Plan	9/01	
Comments Due	10/01	
Draft Final OE Sampling and Analysis Plan	12/01	
Comments Due	1/02	
		-
Draft Track 2 Remedial	2/05	
Investigation/Feasibility Study Report		
Parker Flats and MRS-13B		
Comments Due	8/05	-
	<u></u>	
Draft Final Track 2 Remedial	12/05	
Investigation/Feasibility Study Report	12.00	
Comments Due	3/06	
Comments Duc	.,, 00	
Draft Track 2 Proposed Plan	3/06	
Comments Due	7/06 (4/06)	BCT decision to
Comments Duc	1100 (4:00)	provide additional time
		for DTSC input
·		101 D 1 B 0 mput
Draft Final Track 2 Proposed Plan	8/06 (5/06)	
Comments Due	9/06 (6/06)	
Public Comment Period	10/06 (7/06)	
Tuble Comment 1 criod	10/00 (7/00)	
Draft Track 2 ROD	12/06(7/06)	
Comments Due	1/07 (9/06)	- 14
Comments Due	1101 (3100)	
Draft Final Track 2 ROD	2/07 (9/06)	<u> </u>
Comments Due	3/07 (10/06)	6.
Comments Due	3/07 (10/00)	
Final Track 2 ROD Signed	5/07 (12/06)	66
Final Track 2 ROD Signed	3/07 (12/00)	

Former Fort Ord Property Transfer Document Status Update July 2006

FOST 9 – Track 0 Plug-in Group C, Track 1 and Track 1 Plug-in Parcels (29 Parcels ~1,888 acres)

- FOST complete and signed, 17 parcels (~747 acres) transferred by deed to date.
- Five CRUPs (one per jurisdiction) for 15 parcels (~855 acres) within Prohibition Zone of Fort Ord Special Groundwater Protection Zone:

						Signatures			
CRUP restriction	Parcels	Acres	Recipient	Jurisdiction	DTSC	RWQCB	Army	Status	Notes
				Monterey					
groundwater	2	101.63	FORA	County	Yes	Yes	Yes	recorded	Property transferred.
groundwater	9	199.57	FORA	Marina	Yes	Yes	Yes	recorded	Property transferred.
									DTSC working with
			Veterans Transition						recipient on agreement for
groundwater	2	4.618	Center	Marina	No	Yes	No	final	payment of DTSC's costs.
			California						DTSC working with
		ŀ	Department of	Monterey					recipient on agreement for
groundwater	Ī	476.79	Parks & Recreation	County	No	Yes	No	final	payment of DTSC's costs.
		İ	California						DTSC working with
			Department of						recipient on agreement for
groundwater	_ 1	72.139	Transportation	Marina	No	Yes	No	final	payment of DTSC's costs.

FOST 10 – Track 0 Plug-in Group D, Track 1 Plug-in East Garrison Areas 2 and 4 NE, and Track 1 Plug-in Groups 1 – 5 Parcels (28 Parcels ~719 acres)

- Draft FOST issued for regulatory agency and Army legal review and comment 5/26/2006.
 Army ELD submitted comments on 6/22/2006. USEPA and DTSC submitted comments on 6/27/2006. Groups 1 5 approval memorandum revised, FOST in revision. Start of public comment period for FOST postponed, likely until end of July. Army signature of FOST estimated 9/24/2006.
- Working with DTSC to finalize CRUPs:

						Signatures			
CRUP restriction	Parcels	Acres	Recipient	Jurisdiction	DTSC	RWQCB	Army	Status	Notes
groundwater	7	40.177	FORA	Marina	No	No	No	draft	Submitted to DTSC for review 6/1/06.
groundwater	1	4.545	Monterey- Salinas Transit	Marina	No	No	No	draft	DTSC working with recipient on agreement for payment of DTSC's
residential		4	Samas Hansh	Monterey	INO	INO	INO	uran	Submitted to DTSC for review
excavation	1	63.689 ¹	FORA	County	No	No	No	draft	6/16/06.

¹ The actual area to be restricted is approximately 0.18 of an acre within the parcel.

Former Fort Ord Property Transfer Document Status Update July 2006

FOSL 12 – Military Operations on Urbanized Terrain (MOUT) Site (portion of 1 Parcel ~46 acres)

- FOSL submitted 5/16/2006 for staffing for Army signature. Copies provided to regulatory agencies.
- Army will request a waiver of 10 U.S.C. 2692 from ACSIM for use of munitions on the property by the lessee.

FOSET 5 – ESCA (49 Parcels ~3,478 acres)

- USEPA does not believe the FOSET, in its current form, provides sufficient justification for deferring the CERCLA covenant. DTSC concurs with USEPA comments. Necessary revisions are under consideration.
- OU2 MEC ESD: ESD staffed to Army agencies (AEC, OGC and CHPPM) for review on 6/6/2006. CHPPM and AEC had no comments. OGC provided comments on 7/12/2006.

Fort Ord Munitions Response BCT Meeting Summary of Action Items (June 6, 2006)

Action Item Description

Responsible Party

Due Date

Comments

Site Security/Incident Reports/Detonation:

Field Work/Removal Action Updates/FWVs

c	DTSC comments on Draft MRS-16 Workplan.	Army/DTSC	5/24/2006	Shaw to call Jeff Anderson for clarification. DTSC letter to forward comments by mid next week. (Note: Shaw discussed comments w/ J. Anderson; DTSC comment letter was not issued; draft final Work Plan was issued on 6/2/06).
K	CARB comments on Draft MRS-16 Workplan/Air monitoring plan.	DTSC	6/13/2006	Roman to verify Gary Honcoop received the c mail sent by the Army summarizing the plan for MRS-16.

FFA Schedules and MR RI/FS

	Check for lawyer comments on draft OU2 ESD	-		OU2 ESD was updated and resubmitted on 5/15.
C	Comment on updated draft OU2 ESD.	DTSC	5/26/2006	EPA and RWQCB accepted the updates.
	Complete backcheck of final OU2 ESD			
	CERCLA documentation plan for the remaining areas in R43-48 (SCAs).	Army	Next BCT meeting	Claire to discuss with Bob Carr.
R			(2/23/2006) -	
			(3/16/ 2006)	
, K			(5/18/2006)	
			(6/6/2006)	
			(7/20/2006)	
	Provide FFA schedule for Track 2 RI/FS for Del Rey Oaks sites.	Army	Next BCT meeting	
C			(5/18/2006)	
*			(6/6/2006)	
C	Set up upper-level manager meeting on Track 3 Impact Area RI/FS.	Army/EPA/DTSC	August	Check key participants' calendars next week.
C	Send responses to comments on Track 1 Multiple Sites Groups 1-4.	Army	5/24/2006	
*	Check tracking information for agency hardcopies of Track 1 Approval Memorandum, Multiple Sites, Groups 1-5.	Army	6/7/2006	

^{*} indicates new action item

[&]quot;R" indicates revised action item

[&]quot;C" and gray cells indicate completed items to be withdrawn from list next month

Fort Ord Munitions Response BCT Meeting Summary of Action Items (June 6, 2006)

		Action Item Description	Responsible Party	<u>Due Date</u>	Comments
	~	Provide feedback on proposed description of receptors in the Risk Assessment for Track 3 Impact Area MR RI/FS	EPA/DTSC	6/13/2006	
	π	Provide written comments on draft Track 2 Proposed Plan for Parker Flats Munitions Response Area.	DTSC	6/8/2006	

Property Transfer

Ongoing Actions/Other

	Quarterly Security Program Update	Army	Quarterly	
	Monthly 3-month deliverables schedule review at BCT meetings	All	Monthly	The Army to work on formatting to meet agency needs.
C P	Finalize MR BCT minutes from April 13	Army		The L. C. Waller of Contract o
R	Finalize MR BCT minutes from May 18	Army		In progress.
*	Finalize MR BCT minutes from June 6	Army		

^{*} indicates new action item

[&]quot;R" indicates revised action item

[&]quot;C" and gray cells indicate completed items to be withdrawn from list next month
