

**SUBJECT: MR BCT Meeting**  
**July 20, 2010**  
**10:00 a.m. BRAC Conference Room**

✓	Name	Organization	Phone	E-mail address
✓	Gail Youngblood	Fort Ord BRAC	831-242-7918	<a href="mailto:Gail.youngblood@us.army.mil">Gail.youngblood@us.army.mil</a>
ph	Roman Racca	DTSC	916-255-6407	<a href="mailto:Rracca@dtsc.ca.gov">Rracca@dtsc.ca.gov</a>
PH	Judy Huang	U.S. EPA	415-972-3681	<a href="mailto:Huang.judy@epa.gov">Huang.judy@epa.gov</a>
ph	Lewis Mitani	U.S. EPA	415-972-3032	<a href="mailto:mitani.lewis@epa.gov">mitani.lewis@epa.gov</a>
	David Eisen	COE	831-393-9692	<a href="mailto:David.Eisen@usace.army.mil">David.Eisen@usace.army.mil</a>
	Christopher Prescott	USACE	916-557-7227	<a href="mailto:Christopher.E.Prescott@usace.army.mil">Christopher.E.Prescott@usace.army.mil</a>
	Clinton Huckins	COE	831-884-9932	<a href="mailto:Clinton.j.huckins@usace.army.mil">Clinton.j.huckins@usace.army.mil</a>
✓	Eric Morgan	BLM	831-394-8314	<a href="mailto:eric_morgan@ca.blm.gov">eric_morgan@ca.blm.gov</a>
ph	Stan Cook	FORA	831-883-3672	<a href="mailto:Stan@fora.org">Stan@fora.org</a>
WKC	Bill Collins	Fort Ord BRAC	831-242-7920	<a href="mailto:William.K.Collins@us.army.mil">William.K.Collins@us.army.mil</a>
	Lyle Shurtleff	Fort Ord BRAC	831-242-7919	<a href="mailto:Victor.L.Shurtleff@us.army.mil">Victor.L.Shurtleff@us.army.mil</a>
cn	Chieko Nozaki	Fort Ord BRAC	831-899-7372	<a href="mailto:Chieko.n.nozaki.ctr@us.army.mil">Chieko.n.nozaki.ctr@us.army.mil</a>
ph	Peter Kelsall	Shaw E&I	831-883-5810	<a href="mailto:Peter.Kelsall@shawgrp.com">Peter.Kelsall@shawgrp.com</a>
DJL	Derek Lieberman	Fort Ord BRAC	831-242-4873	<a href="mailto:Derek.S.Lieberman@us.army.mil">Derek.S.Lieberman@us.army.mil</a>

**SUBJECT: MR BCT Meeting**  
**July 20, 2010**  
**10:00 a.m. BRAC Conference Room**

✓	Name	Organization	Phone	E-mail address
PW	Bruce Wilcer	MACTEC E&C	707-793-3887	<a href="mailto:blwilcer@mactec.com">blwilcer@mactec.com</a>
	Mark Eldridge	AEC	410/436-6325	<a href="mailto:Mark.h.eldridge@us.army.mil">Mark.h.eldridge@us.army.mil</a>
KJS	Kevin Siemann	Shaw E&I	831-883-5804	<a href="mailto:Kevin.Siemann@shawgrp.com">Kevin.Siemann@shawgrp.com</a>
OP	Chris Duymich	POM FD	831-242-7901	<a href="mailto:Chris.duymich@us.army.mil">Chris.duymich@us.army.mil</a>
✓	Melissa Broadston	Fort Ord BRAC	831-393-1284	<a href="mailto:Melissa.Broadston@us.army.mil">Melissa.Broadston@us.army.mil</a>
✓	Rob Robinson	Fort Ord BRAC	831-242-7900	<a href="mailto:clinton.w.robinson@us.army.mil">clinton.w.robinson@us.army.mil</a>
✓	Mark Edwards	USACE	242-4828	
JM	Jan Mazer	Shaw	831 883-5800	<a href="mailto:janmazer@shawgrp.com">janmazer@shawgrp.com</a>

MR BCT Meeting Agenda

July 20, 2010

Item	Action	Comment
Site 39 Remediation	Update	
Property Transfer	Update	
ESCA (FORA)	Update	
Fieldwork Update	Update	<ul style="list-style-type: none"> <li>- Units 14/19 work progress</li> <li>- Non-burn areas – work status</li> <li>- Annual inspection of surface removal areas</li> <li>- Range 48 surface removal</li> <li>- Units 15, 21, 32 &amp; 34 status</li> </ul>
Site Security Program	Update	
Remaining RI/FS Areas	Update	<ul style="list-style-type: none"> <li>- Site assessment TM status</li> <li>- E20c.1 status (Track 1)</li> <li>- BLM-HQ (Track 1)</li> </ul>
Track 2 DRO MRA RD/RAWP	Update	
Report Status	Update	
FFA Schedule	Update	
Action Items	Update	
Next BCT meeting	Schedule	<ul style="list-style-type: none"> <li>- September 22</li> </ul>

7/20/2010  
MRBCT

# Fort Ord Military Munitions Response Program Fieldwork Update

7/19/2010

victor.l.shurtleff@us.army.mil

1

# MMRP Fieldwork Update

## PROJECT: MRS-BLM Range 26 (50 acres)

An MMRP action is in accordance with the Track 3 ROD/Range 26 WP in preparation for soil remediation. The area in remediation is located in the southeast portion of MRS-BLM.

Start date: Mar 2010 prep)


Estimated end date : July 2010

PHASES:	Start	End
Vegetation removal - vegetation cutting	03-22-10	04-02-10
MEC Removal		
- Surface remediation	04-09-10	05-11-10
- Subsurface remediation	05-07-10	07-16-10

## ISSUES AND CONCERNS:

- Several areas of anomaly concentrations (attributable to small arms and small metallic debris) interfere with efficient DGM picks. Site 39 FWV 147 adjusted general DGM response level from 14mV to 20 mV to reduce the impact of non-MEC anomaly concentrations on MEC remediation work efficiency.
- Mag and dig process is in use in high anomaly concentration areas where discrete DGM picks are not possible.
- Percent complete

# Status - Range 26

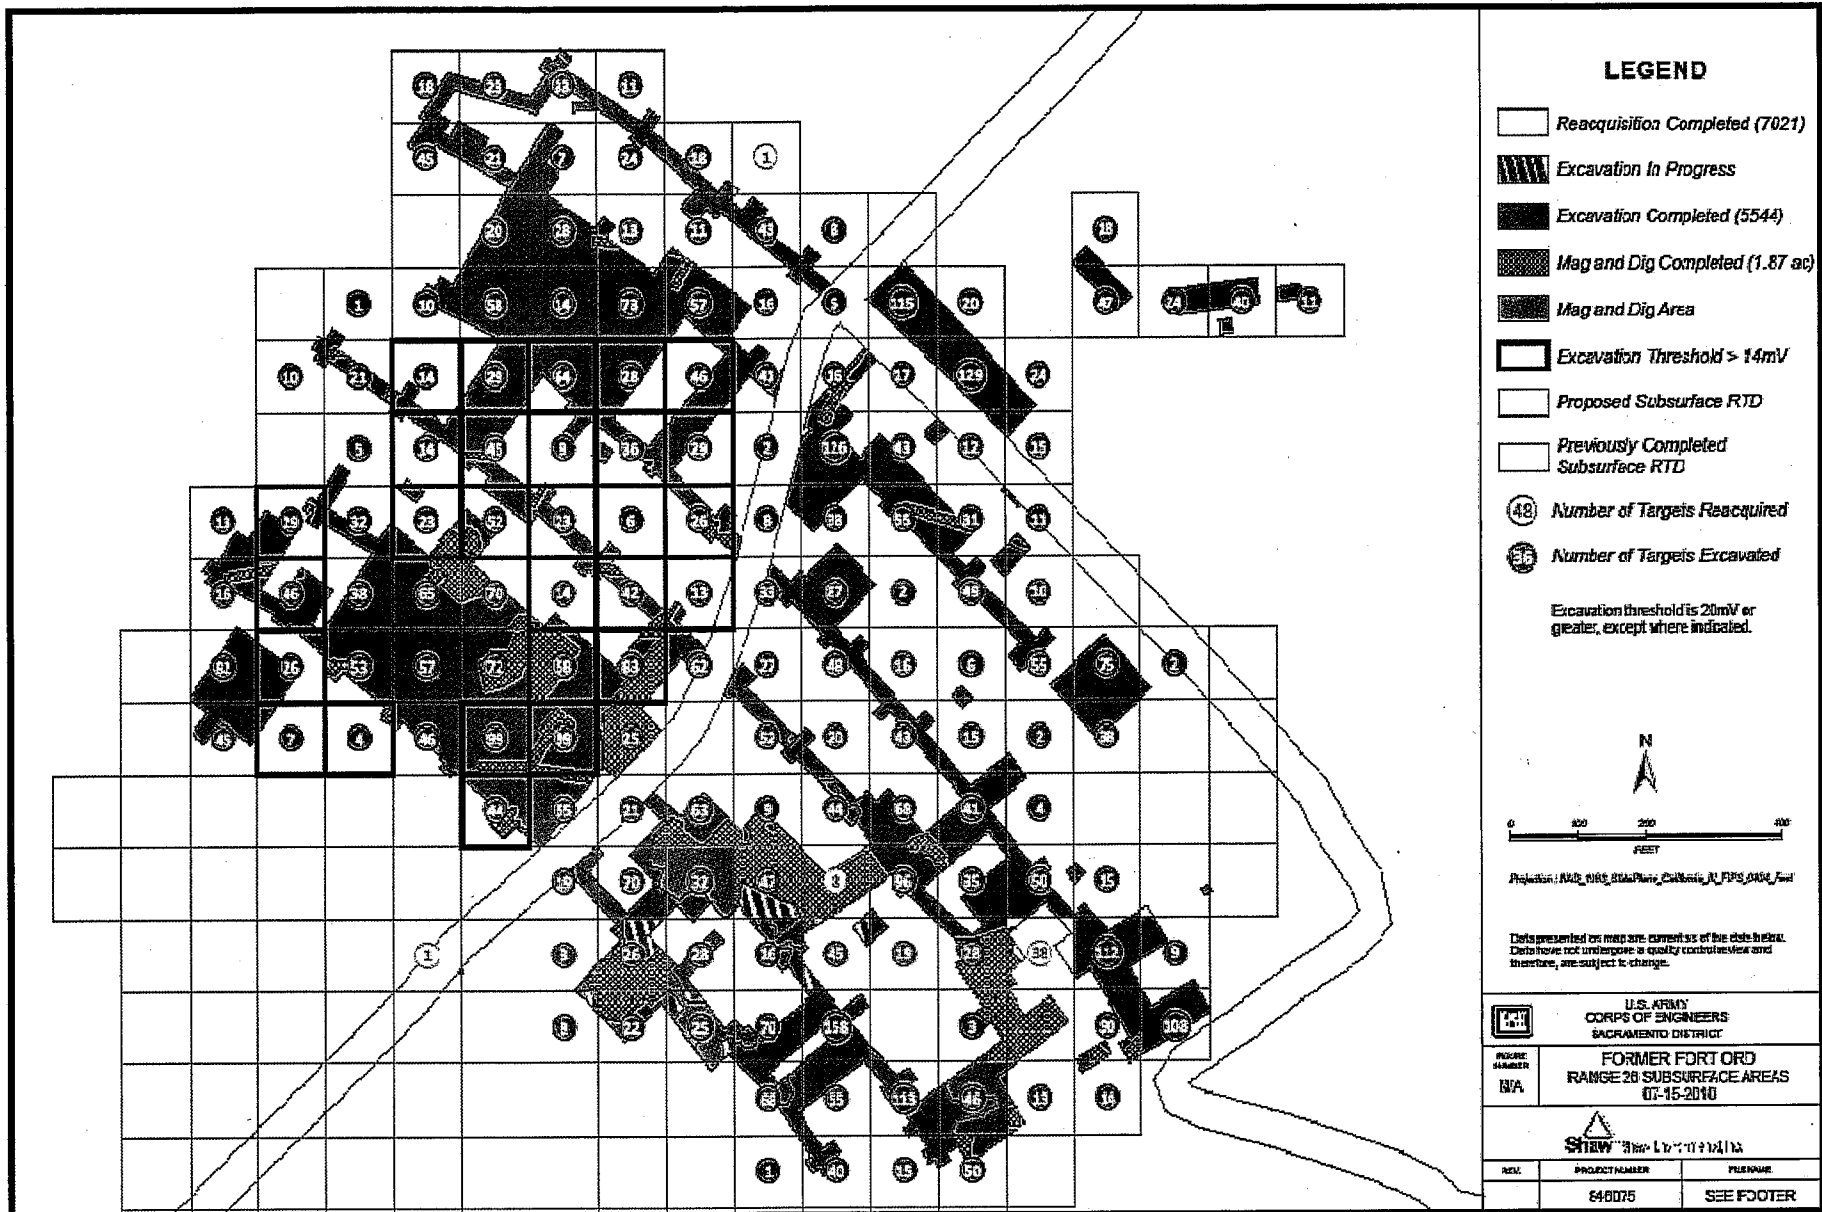

File Path: C:\For\_Ord\_015R26\Proj4\Documents\ProposedRange26\_status.mxd Date: 07/16/10

# MMRP Fieldwork Update

PROJECT: MRS-BLM Unit 15/21/32/34(497 (405 burn) acres)

An MMRP action is in accordance with the Track 3 ROD. The area scheduled for remediation located in the north-eastern portion of MRS-BLM.

Start date: May 2010 (prep)

Estimated end date : July 2011

## PHASES:

	Start	End
Site preparation (fuel breaks/bld. removal)	05-01-10	(07-21-10)

### Vegetation removal

- prescribed burn
- vegetation cutting


### MEC Removal

- Surface remediation
- DGM
- Subsurface remediation, limited

## ISSUES AND CONCERNS:

- Some structures to be demolished and others protected for economy .
- Due to configuration and proximity to protected features, Units 32/34 will be cut to reduce flame height and then burned to support habitat.
- Approx. 40 acres of Unit 32 will not be cut due to habitat or slope.

# Status - Burn Prep MRS-BLM Unit 15/21/32/34

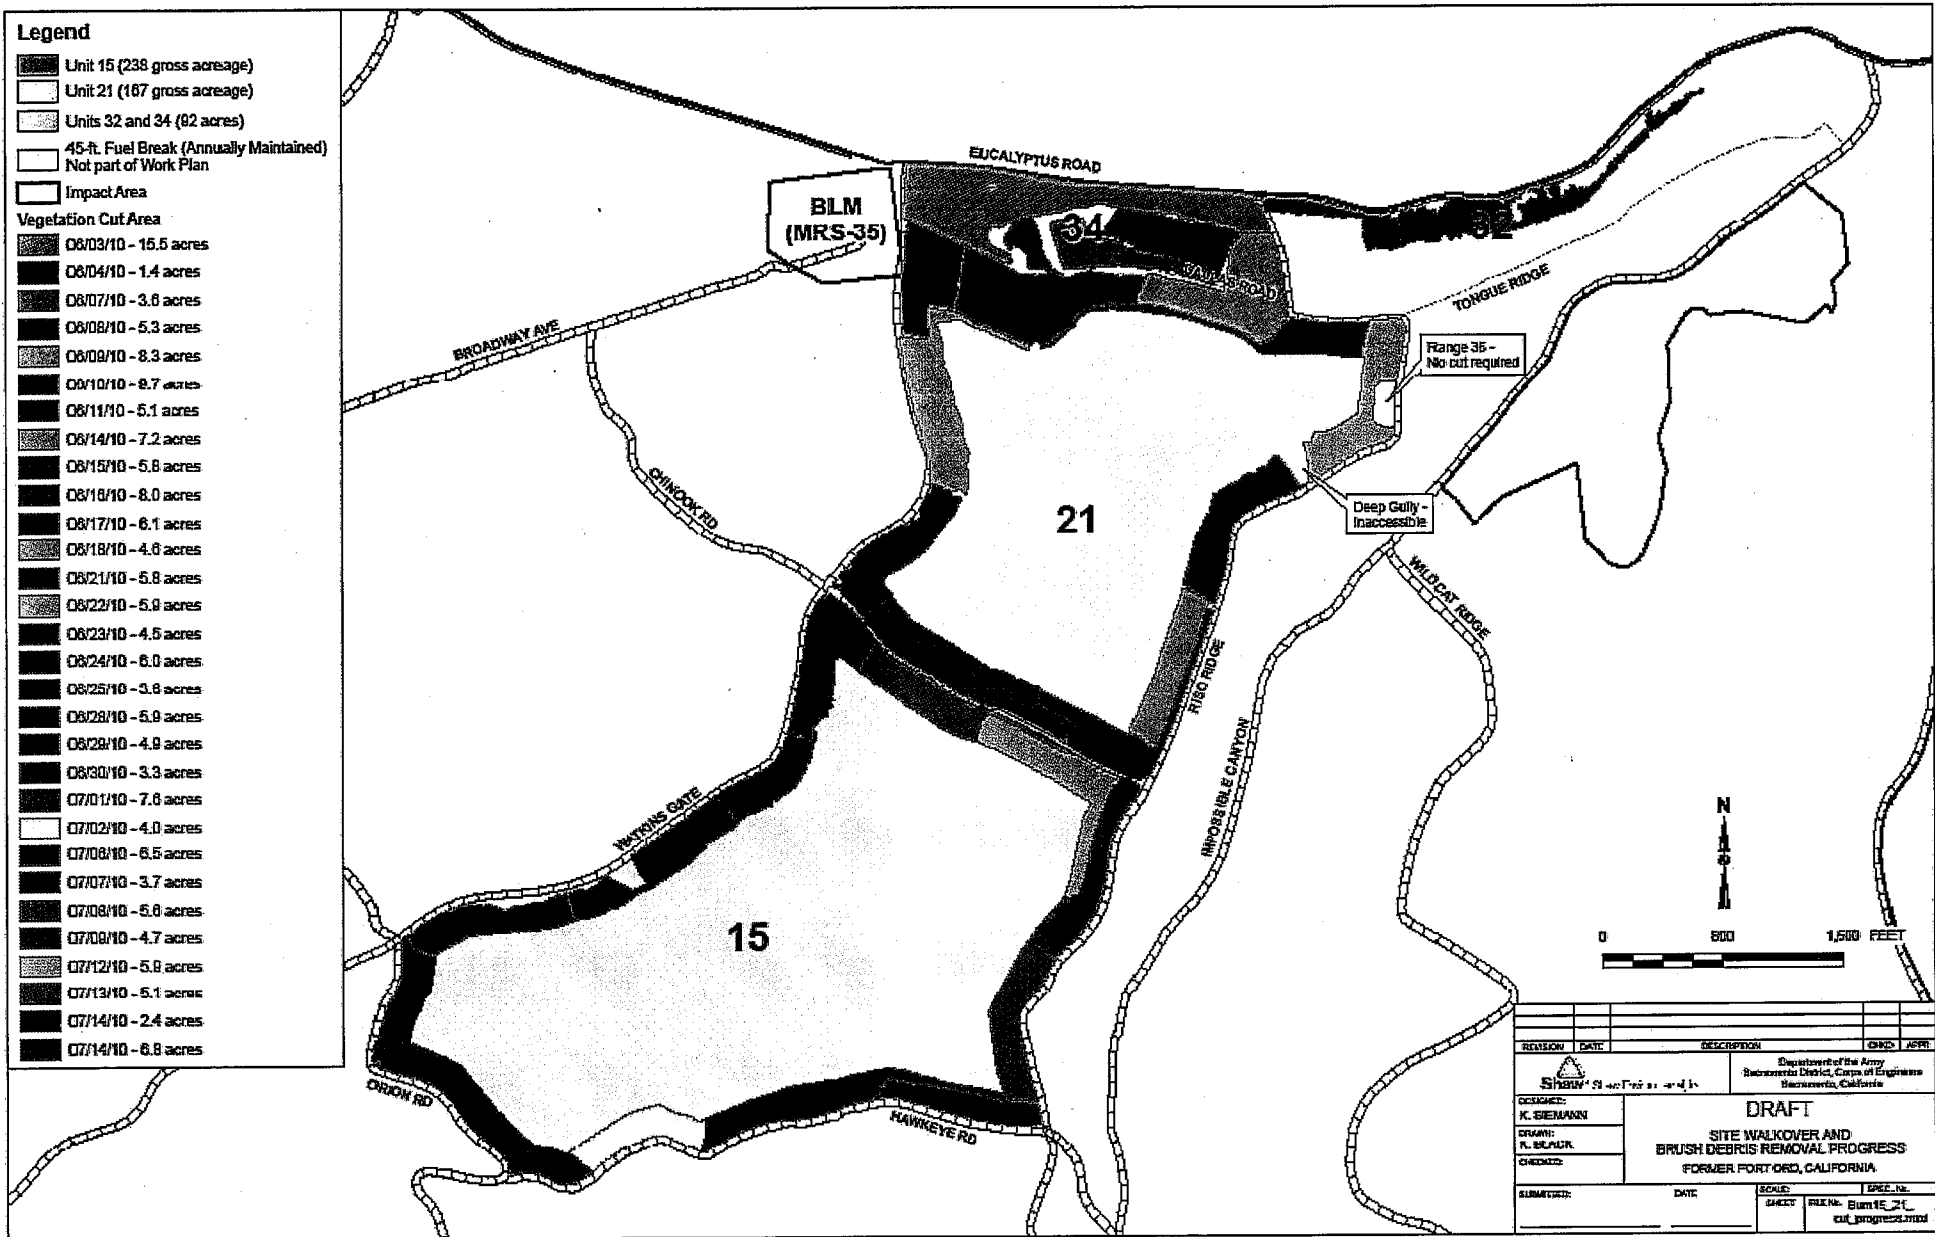



# MMRP Fieldwork Update

Unexploded Ordnance (UXO) / Discarded Military Munitions (DMM) /  
Insufficient Data (ISD), Munitions Debris (MD), and Range Related Debris (RRD)  
Summary

<b>Remediation</b>	<b>UXO/DMM Items</b>	<b>MD lbs</b>	<b>RRD lbs</b>
Rng 26 (subsurface in progress)	8 (unconfirmed)	53	407

# MMRP Site Security Program

- Trespass Incidents:
  - Last 30 days: 0 Year to Date: 1
  
- MEC Incidents:
  - Last 30 Days: 0 Year to Date: 4
  
- Community Education:
  - Total recipients in 2010 to date: 225
  
- MEC Rec and Safety Tng:
  - Total personnel trained in 2010 to date: 68
    - Annual letter offering training to property users and owners, contractors, and public service workers is being staffed and is scheduled to go out in August.
  
- Other:

# U.S. Army Community Outreach Update

---

## Actions:

1. Proposal for letter/update/fact sheet to be distributed to Monterey Bay Estates II residents. Purpose of notification is to discuss results (non-detect) from monitoring well 94 and overall results of off-site Operable Unit 1 groundwater investigation and cleanup.
2. Continued work on interactive map for web site (per Fort Ord Environmental Justice Network comments/requests).
3. Update Fort Ord cleanup section of California State University Monterey Bay web site.

## Recent Activities:

1. June 26, 2010: Hosted the semi-annual community open house / bus tour that emphasized munitions cleanup with a drive around and one stop at the Impact Range. Attended by over 130 people.
2. July 9, 2010 Published Public Notice for FOST 11.
3. Attended Superfund JTI candidates' workshop: July 13<sup>th</sup>. Attended by about 50 people.
4. July 14-15: Hosted the Community Involvement Workshop followed by the Technical Review Committee. Presentations included updates on the Environmental Services Cooperative Agreement, Site 39 and Landfill. Additional poster session was for Administrative Record.
5. On-going: enroll participants in the prescribed burn Direct Notification Program.

## Upcoming Activities

1. July 22 Conduct prescribed burn briefings for officials at California State University Monterey and Monterey County Health Department.
2. Conduct Fort Ord Cleanup tour for staff at Monterey County Health Department (TBD).
3. July 28: Provide Prescribed Burn presentation at the Fort Ord Reuse Authority user's group meeting.
4. July 28: Provide Prescribed Burn presentation at the Fire Chief's meeting.
5. August 13: Provide annual UXO safety briefing for York School.
6. September 3 Participate in an information booth at the Monterey County Fair.

# STATUS: RESPONSE to COMMUNITY COMMENTS (RTC)

AR Number	Title/Subject	Status
OE-0714.3, 6/5/10	Comments submitted by community group - Fort Ord Community Advisory Group on the Draft Track 2 Del Rey Oaks Remedial Design/Remedial Action Work Plan, Former Fort Ord, California	RTC is in progress-collaboration among Army, ESCA and City of Del Rey Oaks.
ESCA-0249.5, 6/10/10	Comments submitted by Mike Weaver of FOCAG on the Draft Group 3 RI/FS Report, Del Rey Oaks / Monterey, Laguna Seca Parking, and Military Operations in Urban Terrain Site MRAs, FORA ESCA Remediation Program	RTC is in progress—ESCA Program.
IAFS-235E.3, 1/15/10	Comments from Mike Weaver [Fort Ord Community Advisory Group] on the Draft Final Work Plan, Historical Area 161 Excavation, Inter-Garrison Training Area, Former Fort Ord, California	RTC is in progress. Part 1: Initial response complete: a letter to CAG noting that we are preparing report/documents that will response to these comments/questions (IAFS-235E.4, 5/4/10). Part 2: Issue draft CWM report-July The initial letter and report will be in the Administrative Record.
OU1-575.2, 4/12/10	Comments submitted by Mike Weaver on the Draft 2009 Annual and Third Quarter Groundwater Monitoring Report, Operable Unit 1, Fritzsche Army Airfield Fire Drill Area, Former Fort Ord, California	The RTC will be incorporated into the Draft Final document. Issue date scheduled for July 21, 2010.
OE-0712.3, 4/23/10	Comments submitted by the Fort Ord Community Advisory Group on the Draft Prescribed Burn 2009 MRS-BLM Units 14 and 19 After Action Report, Former Fort Ord, Monterey County, California	The RTC is complete and included in the Draft Final document. OE-0712B is scheduled for 7/31/10.
OUCTP-0036N.4, 5/20/10	Comments from Mike Weaver [Fort Ord Community Advisory Group] on the Draft Work Plan, Operable Unit Carbon Tetrachloride Upper 180' Aquifer, Former Fort Ord, California	The RTC will be included in Draft Final document.
OU2-676.2, 5/21/10	Comments from Mike Weaver [Fort Ord Community Advisory Group] Draft Annual Report of Quarterly Monitoring, October 2008 through September 2009, Groundwater Monitoring Program, Sites 2 and 12, OU2, and OUCTP, Former Fort Ord, California	RTC is complete and in Volume 1, Appendix G of the Draft Final report. OU2-676A, 8/18/10
OE-0708A.2, 6/4/10	Comments submitted by community group - Fort Ord Environmental Justice Network on the Draft Final MRS-BLM Units 15, 21, 32 and 34 Prescribed Burn Plan	RTC is complete and in the Final document. (OE-078B, 6/30/10)
OE-0708A.3, 6/3/10	Comments submitted by community group - Fort Ord Community Advisory Group Draft Final MRS-BLM Units 15, 21, 32 and 34 Prescribed Burn Plan	RTC is completed and is in the Final document. (OE-078B, 6/30/10)

**07-20-10 Update - Fort Ord Real Estate Actions****FOST 10 deeds:**

1. July 2009 – eight of ten deeds and three CRUPs recorded, 594 acres transferred.
2. Parcel L3.2 (101.19 acres)
  - a. March 2010 – Draft deed reviewed and sent back to USACE, forwarded to FORA for review.
  - b. April 2010 – USACE drafted memorandum to Mr. Whiteford and transmittal to FORA, reviewed by Fort Ord BRAC.
  - c. May 2010 – Monterey County Board of Supervisors approved agreements (license to cross South Boundary Road), covenants and conditions (relating to future use of the property) between the County and York School; York School rescinded its public benefit conveyance (PBC) request; Department of Education withdrew its assignment request.
  - d. June 2010 – FORA and its counsel determining appropriate sequence of transfer.
  - e. July 2010 – FORA submitted EDC MOA amendment to Army for countersignature. Army requested additional supporting documentation.
3. Parcel L23.5.2 (and adjacent FOST 9 Parcel L23.5.1) PBC to Chartwell School.
  - a. June 2010 – Revised information paper supporting assignment to Department of Education submitted to USACE Southwest Division.
  - b. July 2010 – Assignment package sent to DASA for execution.

**FOST 11:**

1. Parcels L2.3 and L2.4.1 in Parker Flats MRA.
2. January 2010 – Army Environmental Law Division (ELD) and Army BRAC review of Draft FOST complete.
3. March 2010 – FOST issued for regulatory agency review.
  - a. Draft MEC-related CRUP also issued to DTSC.
  - b. Two conference calls with USEPA and DTSC: “MEC as a CERCLA hazardous substance” issue, relevant Environmental Condition of Property categorization and CERCLA section.
4. April-May 2010 – Army ELD consulting with OGC.
5. May 2010 – FOST revised based on discussion with OGC and submitted to OGC and ELD for review on May 24.
6. June 2010 – revised FOST issued to USEPA and DTSC for back check. USEPA disagreed with some changes. CRUP issued to DTSC for signature.
7. July 2010 – disagreement resolved, FOST issued for 30-day public comment period (July 10 – August 9).

**FOST 12:**

1. Parcel E20c.1 (fishhook with grenade range) requires Track 1 Plug-in Approval Memorandum (in progress).
2. Parcel E29b.3.1 (Yadon’s piperia) requires completion of biological opinion by USFWS.
3. Parcel S2.1.2 (OU1) requires determination of OPS for OUCTP in the Lower 180-Foot Aquifer.

**FOST 13:**

1. Parcels E8a.1.1.1 and E8a.2 (Fort Ord Landfills) requires completion of Site 39 remedial action and closure of the Landfills.

**FOSET 2 deed amendments:**

1. October 2008 – Five deed amendments issued to FOSET 2 property recipients for signature: Monterey-Salinas Transit (MST), City of Marina, City of Seaside, University of California (UC), and California State University Monterey Bay (CSUMB). Sixth deed amendment for Parcel L37 (City

## **07-20-10 Update - Fort Ord Real Estate Actions**

- of Seaside) not drafted. Some recipients expressed concern about deed amendment language, including the "hold harmless" provision.
2. December 2009 – USACE revised/drafted all six deed amendments using FOSET 5 deed amendments as template. Fort Ord BRAC Office reviewed and commented.
  3. February 2010 – USACE revised deed amendments.
  4. March 2010 – USACE submitted draft deed amendment to FORA for legal review.
  5. April 2010 – FORA completed legal review. USACE issued amendments to recipients for signature April 23.
  6. May 2010 – FORA notified Army the County will require legal descriptions to be attached to the deed amendments. Army issued revised amendments to recipients.
  7. June 2010 – MST and CSUMB signed deed amendments, but CSUMB signed previous draft without legal descriptions. CSUMB agreed to resign the current version. MST deed amendment recorded (Dept of Transportation signed on behalf of the United States). FORA received deed amendments (3) from its counsel and is preparing to sign.
  8. July 2010 – UC signed deed amendment.

### **FOSET 4 deed amendment:**

1. November 2008 – ROD for Del Rey Oaks MRA complete and signed.
2. April 2010 – Preliminary Draft RD/RAWP issued to Army for review. Fort Ord BRAC Office submitted comments, ARCADIS provided responses. Draft RD/RAWP issued to agencies.
3. May 2010 – comments received from USEPA.
4. June 2010 – comment resolution meeting between Army, USEPA, DTSC and Del Rey Oaks. Del Rey Oaks will send letter to DTSC requesting variance to CRUP restrictions; per USEPA CERCLA Warranty cannot be issued until variance to CRUP is complete.
5. July 2010 – Del Rey Oaks drafting letter to DTSC requesting variance to the CRUP.

### **FOSET 5 deed amendment, County North MRA:**

1. March 2010 – draft deed amendment issuing the CERCLA Warranty for County North MRA submitted to USACE for review.
2. April 2010 – USACE preparing signature package. Draft deed amendment forwarded to USACE HQ for review April 21; forwarded to Kutak Rock April 27.
3. July 2010 – Kutak Rock "needs to resolve the issue of whether any action needs to be taken on the CRUP, or otherwise as part of the removal of the restriction in the deed."

### **FOSET 5 deed amendments, Group 3 MRAs:**

1. Five deed amendments issuing the CERCLA Warranty for Group 3 MRAs.

### **University of California FOST 3 and FOST 6 Parcels:**

1. March 2010 – draft deed for Parcels F7.1 (FO-30), F7.2 (FO-31) and S2.1.4.2 submitted to USACE for review.
2. April 2010 – USACE preparing signature package, draft deed submitted to USACE HQ for review.
3. June 2010 – received comments from USACE HQ.
4. July 2010 – draft deed submitted to UC for review.

### **Bureau of Land Management ECOP 2:**

1. Upon completion of applicable Track 1 Approval Memoranda, draft Environmental Condition of Property (ECOP) document for transfer of Track 1 areas to BLM for Army technical and legal review.

**Fort Ord Munitions Response BCT Meeting  
Summary of Action Items (June 25, 2010)**

Action Item Description

Responsible Party

Due Date

Comments

**Property Transfer**

R	FOSETs 2/4/5 CERCLA warranty and deed amendment: the Army will provide EPA and DTSC copies when final.	Army		(May2010) The Army will forward deed amendments for FOSET5 Parker Flats properties. (June2010) Deed Amendments for FOSET5 Parker Flats properties have been provided to the agencies by FORA.
C	Provide legal surveys for FOST11 parcels to the Army.	FORA		(May2010) FOST11 is scheduled for a 30-day public comment period at the end of May. Legal survey info is still needed
*	Forward a backcheck-version of FOST11 for agency review (2 week period).	Army	6/30/2010	(June 2010) Public comment period to begin in July.

**Ongoing Actions/Other**

	Quarterly Security Program Update	Army	Quarterly	
	Monthly 3-month deliverables schedule review at BCT meetings	All	Monthly	The Army to work on formatting to meet agency needs.
	Consider offering an Impact Area hike tour to Fort Ord Users Group, Sustainable Seaside.	Army		(Apr2010) Depends on the outcome of 4/24 tour
C	Review and comment on proposed response to CAG comment on e-mail footers	EPA/DTSC	5/20/2010	
C	Review and comment on draft prescribed burn outreach materials.	EPA/DTSC	5/19/2010	
C	Update the April CIW meeting summary with regard to community comment suggesting that emergency rooms were full during the 2009 prescribed burns.	Army	Next CIW (7/14/2010)	
*	Provide the BCT with a link to the test site for the interactive map of Army cleanup sites.	Army		
*	Check if CSUMB is still using Twitter for student notification.	Army		
C	Finalize MR BCT minutes from March 24	Army	Monthly	
C	Finalize MR BCT minutes from April 13.	Army	Monthly	
	Finalize MR BCT minutes from May 12	Army	Monthly	
*	Finalize MR BCT minutes from June 25.	Army	Monthly	

\* indicates new action item

"R" indicates revised action item

"C" and gray cells indicate completed items to be withdrawn from list next month

**Fort Ord Munitions Response BCT Meeting  
Summary of Action Items (June 25, 2010)**

**Action Item Description**

**Responsible Party**

**Due Date**

**Comments**

**Site Security/Incident Reports/Detonation:**

<b>C</b>	Track MEC safety briefing by BLM; include in site security reporting	Army	5/31/2010	Information will be included in the final site security report.
----------	--	------	-----------	---

**Field Work/Removal Action Updates/FWVs**

<b>C</b>	Show previous investigation data for MRS-BLM Units 13 and 17 for site-specific evaluation	Army	Next meeting (6/25/2010)	
*	Update the burn weather forecast web page	Army	7/1/2010	
*	Provide the prescribed burn program update at the Fort Ord Users' Group meeting.	Army	Next meeting (7/20/2010)	Coordinate with FORA.

**FFA Schedules and MR RI/FS**

<b>C</b>	Check for acceptable timelines for deed/CRUP amendments reflecting ROD modification of LUCs (DRO)	EPA/DTSC	Next meeting (5/12/2010 6/25/2010)	(May2010) The Army will send an e-mail to EPA/DTSC summarizing the issue. (Jun2010) BCT discussion took place 6/24/2010.
*	Update the FFA schedule for Track 2 Del Rey Oaks	Army	6/30/2010	

\* indicates new action item

"R" indicates revised action item

"C" and gray cells indicate completed items to be withdrawn from list next month



## Site 39 Remedial Action Status Update 07/14/2010

### Ongoing Documents

- Issued Final Appendix SSWP (FWV) for Subsurface MEC Removal at HA26.
- Issued Draft Appendix SSWP (FWV) for screening at HA 44 to Agencies.
- Issue Final Appendix SSWP (FWV) for Subsurface MEC Removal on New Surfaces.

### Engineering Activities

#### Site 39

- Completed placement of additional transects.
- Completed 2009-2010 wetland monitoring.

#### OU2 Landfills

- Completed design/grading plan for E/F Hill as borrow source for vegetative cover.

### Construction Activities

#### Site 39

- Surveying, bio clearance, and mowing/limbing
  - Completed HAs 27, 27A, 29, 33, 36, 43, 18, 22, 23, and 19
  - Surveying started at HA 26, 39/40, 44, 48, and 34
- Excavation
  - Completed HAs 27, 27A, 29, 33, 36, 43, 23, 22, 18, and 19
  - Completed over-excavation at HA 19 at four locations
  - Continue excavation at HA 26 -
  - Planning for HA 44 – start date of 7/26..delayed
- Sampling
  - Completed HAs 27, 27A, 29, 33, 43, 22, 23, 18, 36, and 19
  - Collected over-excavation samples from HA 19.
- QC Seeding
  - Recovered all 7 seeds placed to date
  - Placed seeds at HA 26
- Pre-remediation Subsurface Removal
  - HA 26 DGM complete, target requisition and anomaly excavation ongoing
  - Tentative completion date is July 30
- Post-remediation MEC Survey of New Surface
  - Riso Road DGM, target reacquisition, and anomaly excavation completed
  - Planning for DGM and/or mag and dig at low probability HAs
  - Tentative start date of 7/14.
- Planning for HAs 39/40, 28, and 34
- Implement erosion control measures, as needed
- Completed road improvements and repairs for HA 26

#### OU2 Landfills

- Completed Phase 1 vegetative layer removal
- Hauled and placed soil from HA 27, 27A, 29, 33, 36, 22, 23, 43, 18, and 19
- Implement erosion control measures, as needed
- Completed moving 12,000cy soil into Area E and stockpile base rock
- Continue Phase 2 vegetative layer removal

### Technical Memorandum

Tech Memos (TM) will present analytical results with the objective of receiving preliminary concurrence from Agencies that remediation is complete and acceptable and re-contouring/ restoration can occur. (see attached table).

### Technical Memorandum Status Update

HA	Issued to Army for review	Issued to Agencies for review	Comments		
			EPA	DTSC	RWQCB
27	3/12	3/18, 4/12	5/5, add BU	3/22, 5/5	5/4, No Comment
22	4/12	4/12	5/5, No Comment	Ok at BCT	No Comment
43	4/20	4/20	5/5, No Comment	Ok at BCT	4/21, No Comment
36	4/23	4/26, 5/21	5/6, terminology	5/17, 5/26, No Comment	4/26, No Comment
23	5/17	6/4	Ok at BCT	7/13, typo, no comment	6/7, No Comment
33	6/4	6/22	7/6, no comment	7/13, no comment	
27A	7/1	7/6			
29	7/7	7/12			
18	7/9	7/12			
19					

**Site 39 MEC/MD Found**

No.	Munitions Response Site	Burn Unit	Historical Area	Date	Item	Description	Step	Type	Northing	Easting
1	MRS-BLM	1	27	11/04/09	Grenade, hand, practice, M69	Excavation	1	MD	2107999	5738782
2	MRS-BLM	5	29	11/23/09	Projectile, 40mm, practice, M781	Excavation	1	MD	2107895	5744808
3	MRS-BLM	5	29	11/23/09	Cartridge, 40mm, practice, M781	Stockpile	5	DMM	2107345	5744852
4	MRS-BLM	3	23	12/22/09	Grenade, hand, smoke, M18 series	mowing/Excavation	1	DMM	2114089	5734171
5	MRS-BLM	5	29	12/29/09	Cartridge, 40mm, practice, M781	Stockpile	5	DMM	2107345	5744852
6	MRS-BLM	5	29	12/29/09	Cartridge, 40mm, practice, M781	Stockpile	5	DMM	2107345	5744852
7	MRS-BLM	21	36	01/11/10	Projectile, 40mm, practice, M407A1	Outside remediation area	NA	UXO	2119364	5752353
8	MRS-BLM	21	36	01/14/10	Grenade, hand, smoke, white phosphorous, M34	Stockpile	5	MD	2119561	5752435
9	MRS-BLM	21	36	01/27/10	Igniter, time fuse, blasting, M2	Excavation	1	MD	2119410	5752434
10	MRS-BLM	21	36	01/28/10	Grenade, hand, smoke, white phosphorous, M34	Excavation	1	MD	2119420	5752474
11	MRS-BLM	3	23	02/17/10	Cartridge, 40mm, practice, M781	Excavation	1	DMM	2114092	5734157
12	MRS-BLM	Watkins Gate	18	03/04/10	Grenade, hand, training, MK1A1	Excavation	1	MD	2120892	5738150
13	MRS-BLM	2	26	07/12/10	Grenade, hand, practice, M69	Excavation	1	MD	2109628	5736799
14	MRS-BLM	2	26	07/12/10	Signal, illumination, ground, M125 series	Excavation	1	MD	2109635	5736796
15	MRS-BLM	2	26	07/12/10	Projectile, 60mm, mortar, illumination, M83 series	Excavation	1	MD	2109551	5736765

**Site 39 Remediation  
Excavated Volume  
(as of 7/9/2010)**

Summary						
Historical Area	FS Total Plan (bank cy)	Actual Plan To Date (bank cy)	% Planned To Date	OX/SP To Date (bank cy)	Total To Date (bank cy)	Remediation Status
18	2,730	2,730	100%		2,730	complete
18 OVEREX				20	20	complete
22	80	100	100%		100	complete
23	440	440	100%		440	complete
27	120	120	100%		120	complete
27A	1,030	1,030	100%		1,030	complete
27A OVEREX				470	470	complete
27A STOCKPILE				240	240	complete
29	2,580	2,580	100%		2,580	complete
29 OVEREX				330	330	complete
29 STOCKPILE				280	280	complete
33	20	20	100%		20	complete
36	2,750	2,580	100%		2,580	complete
36 OVEREX				40	40	complete
43	150	150	100%		150	complete
19	26,510	26,510	100%		26,510	complete
19 OVEREX		20		20	20	complete
26	24,760	24,760	9%		2,182	
39/40	6,520		0%		-	
48	140		0%		-	
44	3,340		0%		-	
28	6,920		0%		-	
34	26,270		0%		-	
37	19,430		0%		-	
<b>Total</b>	<b>123,790</b>	<b>61,040</b>	<b>49%</b>	<b>1,400</b>	<b>39,842</b>	

**Working Schedule for Site 39 Field Work  
(as of 07/16/2010)**

TASK	HISTORICAL AREA	ACRES	Total Proposed (Bank CY)	Total Excavated (Bank cy)	Pre-Remediation					Remediation							
					Veg Clearance	Surface MEC Removal	DGM	Target Reacquisition	Subsurface MEC Removal	Surveying	Bio Clearance	Mowing/Limbing	Site Prep	Excavation	Over-excavation	Transport to OU2 Landfill	Sampling
1	27	0.1	120	120	NA	NA	NA	NA	NA	10/19	10/28	10/28	11/2	11/2 11/4	NA	1/6	11/18
2	27A	0.6	1030	1740	NA	NA	NA	NA	NA	10/19 10/20	10/29	10/28 10/29	11/4	11/4 11/13	1/4, 1/5, 2/2, 3/31	1/6 1/7, 2/2, 2/3, 4/8	11/19, 1/11
3	29	1.0	2580	3190	NA	NA	NA	NA	NA	10/21	10/29	11/5, 11/9	11/9 11/12, 11/16	11/17 12/1	1/6	12/28- 12/31, 1/6, SP on 2/2	12/2, 1/12, SP on 2/9,
4	OU2 Landfill Phase 1				NA	NA	NA	NA	NA	10/27	NA	11/9 11/12	12/1	12/2, 12/31, 1/11	NA	NA	NA
5	36 (Explosives)	0.51	2750	2790	NA	NA	NA	NA	NA	10/22	12/10	12/24	1/11	1/12 2/1	3/22	1/12 2/1, 3/22	2/9, 3/22
6	43	0.1	150	150	NA	NA	NA	NA	NA	10/20	10/26	NA	2/2	2/8 2/9	NA	3/16	2/9, 2/23
7	33 (Explosives)	0.01	20	20	NA	NA	NA	NA	NA	10/20	12/10	12/24	1/27	1/27	NA	1/27	2/9
8	OU2 Landfill Phase 1				NA	NA	NA	NA	NA	NA	NA	NA	NA	2/16 3/4	NA	NA	NA
9	Austin Stockpile				NA	NA	NA	NA	NA	NA	12/10	12/21	2/1	NA	NA	NA	NA
10	22	0.1	80	80	NA	NA	NA	NA	NA	10/20	10/26	12/22	2/4	2/9 2/10	NA	3/16	2/23
11	23	0.3	440	440	NA	NA	NA	NA	NA	10/22 & 10/26	12/10	12/22	2/4	2/10, 2/16-17	NA	3/16	2/23
12	18	1.4	2730	2750	NA	NA	NA	NA	NA	10/26-27, 12/3, 12/8-	12/21, 2/4	1/8, 1/11, 2/4,	2/16	2/17 3/4	3/4	3/16 3/23	3/4, 3/9, 3/31, 4/20
13	19	13.8	26510	26530	NA	NA	NA	NA	NA	12/16 2/3	2/8, 3/4	2/16 3/11	3/8 3/16	3/17 5/13	6/24, 6/28	3/24 5/24	4/13 - 5/26, 6/28
14	OU2 Landfill Phase 2				NA	NA	NA	NA	NA	10/27	NA	NA	NA	5/17 7/22	NA	NA	NA
15	26	13.9	24760	2182	3/3 3/30	4/8 4/23	4/12 4/30	5/3 7/2	5/10 7/30	6/14 8/5	3/3, 5/17	NA	5/4 6/28	6/28 9/16		7/12 9/16	8/2 9/23
16	39/40	2.5	6520		NA	NA	NA	NA	9/13 10/21	5/17 (ex)	7/14	7/19 7/22	9/6 9/9	9/13 10/21		9/13 10/21 (1X/wk)	9/27 10/28
17	44	1.8	3340		7/8, 9	8/6	NA	NA	8/9 9/10	5/17 (ex)	5/25, 6/15, 7/7	7/8, 9	8/2 8/6	8/9 9/10		8/9 9/10	9/10
18	48	0.05	140		7/26 7/27	7/26 7/27	NA	NA	7/26 7/27	5/17	6/3 6/10	NA	7/26 7/27	7/26 7/27		7/26 7/27	7/28
19	28	3.2	6920							6/14 (ex)							
20	34	7.9	26270							5/18 (ex)							
21	37	6.2	19430														
<b>Total</b>		<b>53.5</b>	<b>123790</b>	<b>39992</b>													

Notes:  
11/17 date completed  
11/18 tentative scheduled start and end dates  
11/23
